BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	: Executive Engineer Byatarayanpura Division
Project Name	: Package No.02 (Package Consists of 21 Works)
Consultants	: Rashtrotthana Consultants
Project Manager /Team Leader	: Karthik Reddy
Project Start Date	: 23-Oct-18
Project End Date	: 22-Oct-19
Project Length in Months	: 12 months

Sl. No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
3	Removing and refixing stone slabs of drains and pointing in CM (1:3) as per the directions of the Engineer-in-charge of the work	Sqm	7225.02	7225.01	100	24-10-18	08-06-20	593
4	Providing granite slabs of selected quality roughly dressed hereof a size of 7.5 cms thick and fixed in cement mortar (1:4) including fixing curing etc.,	Sqm	1805.18	1805.18	100	24-10-18	08-06-20	593
6	Earthwork excavation by manual means in ordinary soil involving an average horizontal throw upto 3meters and an average lift upto 1.5 m, excavated surface leveled and sides neatly dressed.	Cum	9966.47	8086.04	81	24-10-18	08-06-20	593
8	Excavation for roadwork in soil with hydraulic excavator of 0.90 cum bucket capacity including cutting and loading in tippers, trimming bottom and side slopes.	Cum	3031.37	1380.16	46	05-11-18	11-06-20	584
9	Lead for disposal of earth shall be paryable at Carriage rates (Lead & Lift) by mechanical means including loading and unloading up to 1Nano	Cum	19372.14	15840.30	82	24-10-18	02-07-20	617
11	Providing,laying, spreading and compacting crushed stone aggregates of granite/trap basalt to wet mix macadam specification	Cum	5773.44	4890.78	85	08-11-18	06-07-20	606
12	Scarifying bituminous course 50mm to 75mm thick along with pervate carpet / surface dressing by road roller attached with scarifier without disturbing the base and stacking the debris including cost of all labour charges,	Sqm	8449.88	7101.71	84	03-11-18	16-06-20	592
14	Providing and applying primer coat with 3lt bitumen emulsion on prepared surface of granular Base such as WBM WMM including clearing of road surface and spraying primer at the rate of 0.60 kg/sqm using mechanical means	Sqm	24705.56	21135.32	86	12-11-18	11-07-20	607
16	Providing and laying dense graded bituminous macadam using crushed aggregates of specified grading, premixed with VG30 grade bituminous binder and, transporting the hot mix to work site,	Cum	356.58	178.06	50	12-11-18	11-07-20	607
17	Cleaning the existing black topped surface with brooms,soft brushes and finally dusting with old gunny bags and/or compressed air to receive bituminous treatment including cost of all materials,	Sqm	85574.84	82480.64	96	19-11-18	13-07-20	603
18	Providing and applying tack cost using 80/100 grade bitumen (VG10) on prepared black topped surfaces	Sqm	93484.60	87315.37	93	20-11-18	13-07-20	601
19	Providing and laying bituminous concrete 30-40 mm compacted thickness	Cum	3938.28	3691.31	94	20-11-18	13-07-20	601
20	Road Marking with Hot Applied Thermoplastic Compound with Reflectorising Glass Beads on Bituminous Surface	Sqm	3461.99	3259.51	94	24-11-18	18-07-20	602
22	Cement concrete pavement.Construction of un-reinforced plain cement concrete pavement, thickness as per design,	Cum	823.99	823.99	100	24-11-18	18-07-20	602
31	Dismantling of existing structures like culverts, bridges, retaining walls and other structure comprising of masonry, cement concrete, wood work, steel work,	Cum	472.83	472.83	100	19-11-18	24-06-20	583
32	Providing and laying in position plain cement concrete of mix 1:3:6 with OPC cement @ 220kgs, with 40mm and down size graded granite metal coarse	Cum	1059.80	978.64	92	20-11-18	16-07-20	604
33	Providing laying plain/ reinforced cement concrete M20 Grade for Box Culvert walls of thickness 10cm to 30cm including centering shuttering for work etc.	Cum	935.42	756.98	81	26-11-18	22-07-20	604
34	Providing TMT steel reinforcement for R.C.C work including straightening, cutting, bending, hooking, placing in position, lapping and / or welding wherever required.	Tonne	56.05	42.04	75	22-11-18	20-07-20	606
35	Vaccum de-watering with vaccum pump and suction mat and compaction with skin floater clubbed with floating disc including cost of generator,	Sqm	4955.99	4956	100	24-11-18	18-07-20	602
39	Providing and laying in position plain cement concrete of mix 1:2:4 with cement @ 2.6kgs, with 20mm and down size	Cum	62.12	62.12	100	20-12-18	27-07-20	585
5	Supplying and fixing M.S. Rectangular poles made out of 3 equal angles of 63x63x6 mm welded together and fixed in CC (1:2:4) WITH 2 NOS 16mm dia M.S.	Sqm	305.00	305.00	100	20-12-18	27-07-20	585

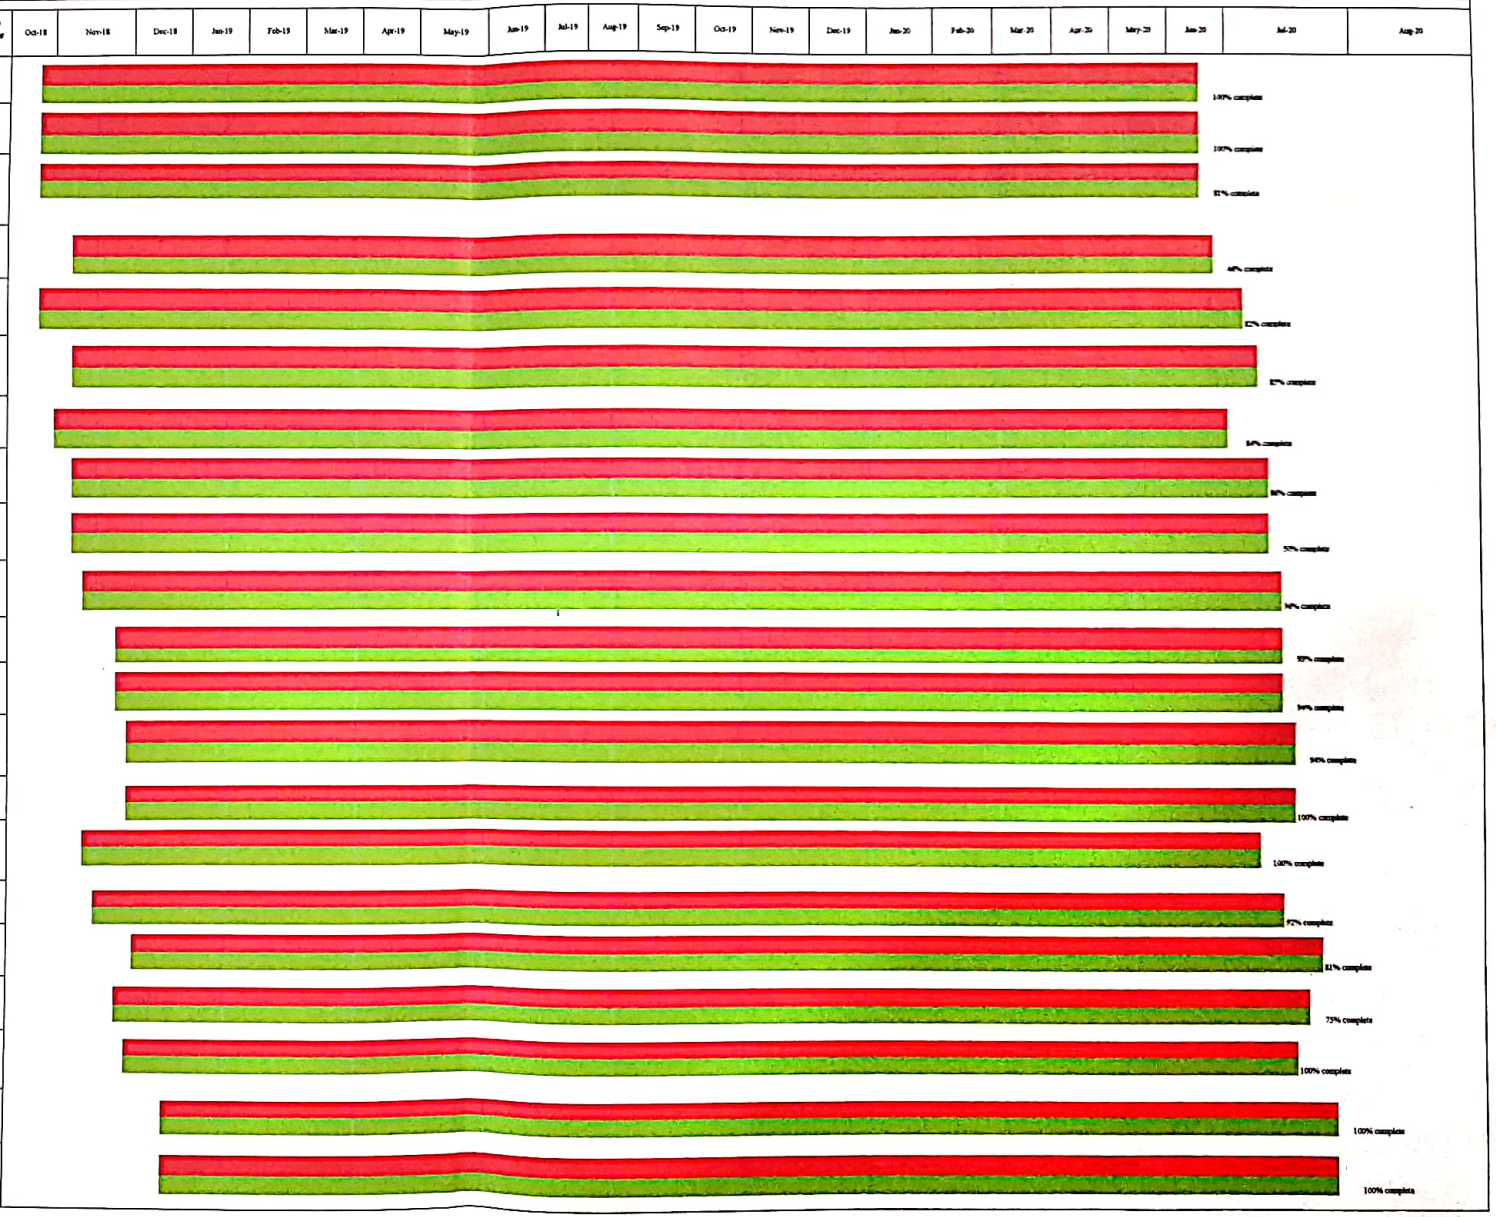

SRAPRASAD CONSULTANTS BANGALORE

Assistant Executive Engineer
Kodigehalli Sub Division
BBMP, Bangalore

Scanned by CamScanner

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Byatarayanapura Division
Project Name	:	Package No 02 (Package Consists of 11 Works)
Consultants	:	Padmprasad Consultants
Project Manager /Team Leader	:	Karthik Reddy
Project Start Date	:	22-Oct-18
Project End Date	:	22-Oct-19
Project Length in Months	:	12 months

Sl. No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
44	Providing chain link fencing 50mm size of 8 gauge properly stretched between existing rectangular poles and fixed with suitable bolts & nuts.	Sqm	592.50	592.50	100	24-12-18	30-07-20	584
45	Providing and fixing M.S. Block pape of 10mm dia, of heavy guage of 14 including removing the bends, cutting the pape, and fixing pape in between the existing two verticle poles	Rmt	553.80	553.80	100	22-12-18	29-07-20	585
E3	Providing and fixing M.S. Gate as per Chief Architect Drawing, using 50mm x 50mm 14 guage M.S	Sqm	18.38	18.38	100	27-12-18	01-08-20	583
E4	Providing and applying enamel metal paint two coats (excluding priming coat) over new steel or other metal surface	Sqm	36.75	36.75	100	28-12-18	03-08-20	584

Assistant Executive Engineer
Kodigehalli Sub Division
BBMP, Bangalore

PADMPRASAD CONSULTANTS BANGALORE

Scanned by CamScanner
